

ASSAM LEGISLATIVE ASSEMBLY
STARRED QUESTION NO: 267
DATE OF REPLY- 29/07/2026

Subject : Implementation and Enquiry into XIV Finance Commission Works in Mohammadpur Joykrishnapur GP.

MLA : Shri Zubair Anam Mazumder :

Will the Minister of Panchayat & Rural Development Department be pleased to state :

- (a) Whether the following works were sanctioned and executed under the XIV Finance Commission Grants in Mohammadpur Joykrishnapur Gaon Panchayat, Hailakandi District:
 - i) Guard Wall on the south side of the Auditorium building, Mahammadpur Part-II;
 - ii) RCC Guard Wall for the Community Water Pond near the house of Rahim Uddin; and
 - iii) Renovation of Community Pond with Guard Wall near the Railway Line (Phase-II);
- (b) If so, furnish the sanctioned amount, implementing agency, executing agency, completion date and present status of each work?
- (c) Whether any complaint, audit objection or enquiry, including Magistrate-level enquiry, has been initiated regarding the above works. If so, furnish the findings and action taken.
- (d) Whether the Government has verified that the works were executed at the approved locations and are serving the intended public purpose.
- (e) Whether any financial irregularity, deviation or misutilisation of XIV Finance Commission funds has been detected. If so, furnish the details and action taken.

REPLY

Shri Atul Bora, Hon'ble Minister, Panchayat & Rural Development will reply:

- (a) As per information received from the Office of the Hailakandi Zilla Parishad, the works namely (i) 'Guard Wall on the south side of the Auditorium Building, Mahammadpur Part-II' and (ii) 'RCC Guard Wall for the Community Water Pond near the house of Rahim Uddin' were taken up under the 14th Finance Commission Grant. However, the work of (iii) 'Renovation of Community Pond with Guard Wall near the Railway Line (Phase-II)' was taken up under the 15th Finance Commission Grant.
- (b) As per information received from the Office of the Hailakandi Zilla Parishad, the sanctioned amount, implementing agency, executing agency, completion date and present status of each work is furnished below:

Name of Scheme	Sanctioned Amount	Implementing Agency	Executing Agency	Completion Date	Present Status
Guard Wall on the south side of the Auditorium Building, Mahammadpur-II (14th FC)	₹ 5.50 (L)	Mahammadpur Joykrishnapur GP	Mahammadpur Joykrishnapur GP	12-03-2019	Work completed
RCC Guard Wall of the Community Water Pond near the house of Rahim Uddin (14th FC)	₹ 4.00 (L)	Mahammadpur Joykrishnapur GP	Mahammadpur Joykrishnapur GP	10-03-2019	Work completed
Renovation of Community Pond with Guard Wall near the Railway Line (Phase-II) (15th FC)	₹ 3.75 (L)	Mahammadpur Joykrishnapur GP	Mahammadpur Joykrishnapur GP	05-04-2023	Work completed

- (c) As per information received from the Office of the Hailakandi Zilla Parishad, complaints were received and accordingly a Magistrate-level enquiry was conducted by the District Commissioner's Office, Hailakandi. The enquiry report is annexed at **Annexure-A**.
- (d) As per the Inquiry Report dated 22nd May, 2026 submitted by Dr. Raj Prasanna Aleman, Assistant Commissioner cum Executive Magistrate, Office of the District Commissioner, Hailakandi; the three no. of schemes namely (i) Guard Wall on the south side of the Auditorium Building, Mahammadpur part-II (ii) RCC Guard Wall of the Community Water Pond near the house of Rahim Uddin and (iii) Renovation of Community Pond with Guard Wall near the Railway Line (Phase-II) were taken up for the inquiry for alleged misappropriation of fund.

The findings of the Inquiry Report are stated below –

- (i) With regard to scheme “Guard Wall on the south side of the Auditorium Building, Mahammadpur-II” it is stated in the Inquiry Report that the Guard Wall on the south side of Auditorium Hall at Mahammadpur Part-II is physically present at the site and is verifiable on ground. It is further stated that the Auditorium Hall lies near the personal residence of Ex-MLA, Katlicherra LAC, so the Guard Wall constructed on south side also covers the MLA’s personal residence. No financial irregularities have been detected.
- (ii) With regard to the scheme “RCC Guard Wall of the Community Water Pond near the house of Rahim Uddin”; it is stated in the Inquiry Report that the RCC Guard Wall for Community Water Pond is physically present at the site and that the Community Pond lies within close proximity of the Ex-MLA, Katlichera. It is further stated that the Community Pond is being used by locals. No financial irregularities have been detected.
- (iii) With regard to the scheme “Renovation of Community Pond with Guard Wall near the Railway Line” it is stated in the Inquiry Report that the RCC Guard Wall for Community Water Pond at Mahammadpur-2 is physically present at the site and that the Community Pond lies within close proximity of the Ex-MLA, Katlichera. It is further stated that the Community Pond is being used by locals. No financial irregularities have been detected.

Copy of the Inquiry Report is annexed at **Annexure-A**.

- (e) No financial irregularity, deviation or misappropriation of XIV Finance Commission funds has been detected as per the Magistrate-level Inquiry Report annexed at **Annexure A**.

(Replies and enclosures have been uploaded in the www.cms.neva.gov.in portal)

14907
10/06/26

ADC (Panchayat)

PLZ forward to P&RD Deptt
for n/a**ANNEXURE-A**

GOVERNMENT OF ASSAM

OFFICE OF THE DISTRICT COMMISSIONERHAILAKANDI

Dated- Hailakandi the 22nd May, 2026To,
The District Commissioner,
Hailakandi.

Sub- Submission of Enquiry Report

Sir,

With reference to the subject cited above and in continuation of the letter received from your office vide reference no. ECF 3712/203, I hereby submit the enquiry report regarding the alleged misappropriation of Government Funds in Katlicherra LAC.

This is for your kind information and necessary action.

Enclosed- as stated above(5 schemes in question)

Yours' faithfully,

Dr. Raj Prasanna Aleman

Dr. Raj Prasanna Aleman

(Assistant Commissioner cum Executive
Magistrate)



GOVERNMENT OF ASSAM
OFFICE OF THE BLOCK DEVELOPMENT OFFICER
LALA DEVELOPMENT BLOCK

Estimate

DISTRICT	:- HAILAKANDI
Name of G.P.	:- Mahammedpur Joykrishnapur G.P
Name of Block	:- Lala Development Block
PROGRAMME	:- 14th Finance Commission 2018-19 (1st & 2nd. inst.)
NAME OF WORKS	:- Construction of Guard wall South side of Auditorium Hall at vill.- Mahammedpur pt.- II. (Group – 03).
ESTIMATED COST	:- Rs. 550000.00

GOVERNMENT OF ASSAM
OFFICE OF THE BLOCK DEVELOPMENT OFFICER
LALA DEVELOPMENT BLOCK

Name of District :- Hailakandi
 Name of Block :- Lala Development Block
 Name of G.P. :- Mahammedpur Joykrishnapur G.P.
 Name of work :- Construction of Guard wall South side of Auditorium Hall at
 vill.- Mahammedpur pt.- II. (Group -- 03).
 Estimated Amount :- 550000.00


Report

It is essential to provide Guard wall for proper protection facilities for road protection of valuable area. The Scheme has been taken up in Goan Sobha under 14th Assam financial Commission.

As per Instruction of higher Authority the Estimate has been framed to show the probable cost of the work. As per as possible work will be executed by engaging local labour to assist them financially in this Hen Season.

The rate of this estimate has been quoted from SOR 2013-14 APWD(Building) and SOR (RR) PWRD Assam 2018-19. As trend of GST a premium of 7% has been added as per the latter of Superintending Engineer P.W.D Building, Silchar Circle. As per norms 10% being deducted as Contractor's profit & 2% is added as Contingency.

All the works will be carried out as per A.P.W.D general specifications current in the state, following all the Guidelines of 14th F.C and by observing all instructions and formalities of the P&RD department time to time


 BDO Lala Dev. Block


 GP Secy.


 A.E. / S.E. / A.E. Engineer
 Lala Dev. Block

GOVERNMENT OF ASSAM
OFFICE OF THE BLOCK DEVELOPMENT OFFICER
LALA DEVELOPMENT BLOCK

DETAILS OF ABSTRACT

Name of Scheme :- *construction of guard wall south side of*
Auditorium Hall at vill - Mahammelpur - II
(Group - 3)

1. Construction of Guard wall.....	Rs. 462900.00
	T Rs. 462900.00
Add 20 Percent Extra Caring Charge (+)	Rs. 92580.00
	T Rs. 555480.00
Deduct 10% being contractors profit (-)	Rs. 55548.00
	T Rs. 499932.00
Add cost of sign board	(+) Rs. 4000.00
	T Rs. 503932.00
Add 7% GST	(+) Rs. 35275.00
	T Rs. 539207.00
Add 2% contingency	(+) Rs. 10784.00
Grand Total	Rs. 549991.00


Say Rs. 550000.00

(Rupees Five lakh Fifty thousand) only.


 BDO Lala Dev. Block


 GP Secy.


 JE / A.E.
 Credited Engineer
 Lala Dev. Block

550000
Five lakh fifty thousand only
148 PC/M Jyoti Chakraborty / 18-19/147


GOVT. OF ASSAM

Dist- Hailakandi

ZP- Hailakandi

Detail estimate of Guard Wall (Length= 50.00m and Height=1.20m)

Name of Work:-

Construction of Guard Wall South side of Auditorium Hall at vill.- Mahammedpur pt.-II.
(Group - 03)

Item No	Particulars	No	L	B	H	Qty	Unit	Rate (Rs.)	Amount
1/1.1	Earthwork in excavation in foundation structures of wall, column etc. including refilling after completion of work								
	Footing	26.00	1.50	1.50	1.75	102.38			
	Tie Beam	1.00	50.00	0.25	0.25	3.13			
	(-)Deduction for Post	26.00	0.25	0.25	0.25	0.41			
						105.09	Cum	108.82	11436.30
2/4.1.1	Providing soling in foundation and under floor with stone/best quality picked jama brick sand pack and laid to level in panel after preparing the sub grade as directed including all labour and materials and if necessary dewatering complete.(Flat brick soling)								
1									
(Civil SOR 2013-14)									
	Footing	26.00	1.50	1.50		58.50			
	Tie Beam	1.00	50.00	0.25		12.50			
	(-)Deduction for Post	26.00	0.25	0.25		1.63			
						69.38	Sqm	368.71	25579.26

3/11 4 Providing concrete for plain/reinforced concrete in open foundations complete as per drawings and technical specifications Clause 802, 803, 1202 & 1203
B) With natural Gravel
III) P C C Grade M20
Nominal Mix 1 2 4 (Hand Mix)

Footing	26 00	1 50	1 50	0 07	4 33		
Tie Beam	1 00	50 00	0 25	0 07	0 93		
(-)Deduction for Post	26 00	0 25	0 25	0 07	0 12		
					5 13	Cum	5543 90 28461 00

4/12 8 Supplying, fitting and placing TMT (Fe-500 D) reinforcement bar (From Primary Producer TATA/SAIL/Essar Steel/Jindal steel/Shyam steel/RINL) in substructure complete as per drawings and technical specification Clauses 1002, 1005, 1010 & 1202

Tie Beam 12mm dia	1 00	50 00	4 00	0 89	176 00		
Post 12mm dia	26 00	2 00	4 00	0 89	185 12		
Footing Base 10mm dia @ 100mm c/c	26 00	1 35	28 00	0 82	608 34		
8mm stirrups for Beam @ 125mm c/c	1 00	401 00	0 90	0 40	142 56		
8mm stirrups for Post @ 125mm c/c	26 00	13 00	0 78	0 40	105 46		

1220 47

Add 5% for Lappage 1281 49 Kg

1 28 Ton 56373 70 72242 38

5/12.5	Plain/reinforced cement concrete in substructure complete as per drawings and technical specification Clauses 802, 804, 805, 806, 807, 1202 and 1204 A) With crushed stone IV) R.C.C grade M 20					
	Tie Beam	1.00	50.00	0.25	0.25	3.13
	Post	26.00	0.75	0.25	0.25	1.22
	Trapezoidal Section	26.00	0.58	1.45	0.25	5.44
	Footing Base	26.00	1.45	1.45	0.35	19.13
					28.91	Cum 7073.00 204490.86

6/13.2	Supplying, fitting and placing TMT (Fe-500D) reinforcement bar . (From Primary Producer :TATA/ SAIL/ EsserSteel/Jindal steel/Shyamsteel/RINL) in superstructure complete as per drawing and technical specifications Clauses 1002, 1010 and 1202					
	Post 12mm dia	26.00	1.20	4.00	0.89	111.07
	8mm stirrups for Post@125mm c/c	26.00	11.00	0.43	0.40	48.58
					159.65	Kg
				Add 5% for Lappage	167.63	Kg
					0.17	Ton 57715.00 9674.86

7/13.1	Providing and laying reinforced cement concrete in super structure as per drawing and technical specifications Clauses 800, 1205.4 and 1205.5 A) With crushed stone II) R.C.C Grade M20					
	Post above Tie Beam	26.00	0.15	0.15	1.20	0.70
					0.70	Cum 7679.55 5391.04

8	Providing formwork of ordinary timber planking so as to give a rough finish including centering, shuttering, strutting and propping etc. and removal of the same of in-situ reinforced concrete and plain concrete work in; (Using 25mm Tie Beam						
		2.00	60.00	0.26	26.00		
	Post	104.00	0.76	0.26	10.60		
		104.00	1.20	0.16	16.72		
	Trapezoidal Section	104.00	1.46	0.26	37.70		
	Base	104.00	1.46	0.36	62.64		
					163.66	8qm	262.24 36732.66


9/11.6	Brick masonry work in cement mortar in foundation complete excluding pointing and plastering as per drawing and technical specifications Clauses 600, 1202 & 1203						
	1. Brick masonry in 1:3 cement mortar	1.00	50.00	0.13	1.20	7.50	
	(-)Deduction for Post	26.00	0.15	0.16	0.13	0.08	
						7.42	Cum 6807.30 50525.16

10/12.3	Plastering with cement mortar (1:4), 15 mm thick on brick work in substructure as per technical specification Clauses 613.4 & 1204						
	Brick Wall	2.00	50.00	1.20	120.00		
		1.00	50.00	0.13	6.25		
					126.25	sqm	129.57 16358.21
Total Cost of Civil works of Guard Wall						462891.63	
Say(Rs.)						462900.00	

BDO Lala Dev. Block
BLOCK DEV. OFFICER
LALA DEV. BLOCK

GP Secy.


Asst. Engineer
Lala Dev. Block

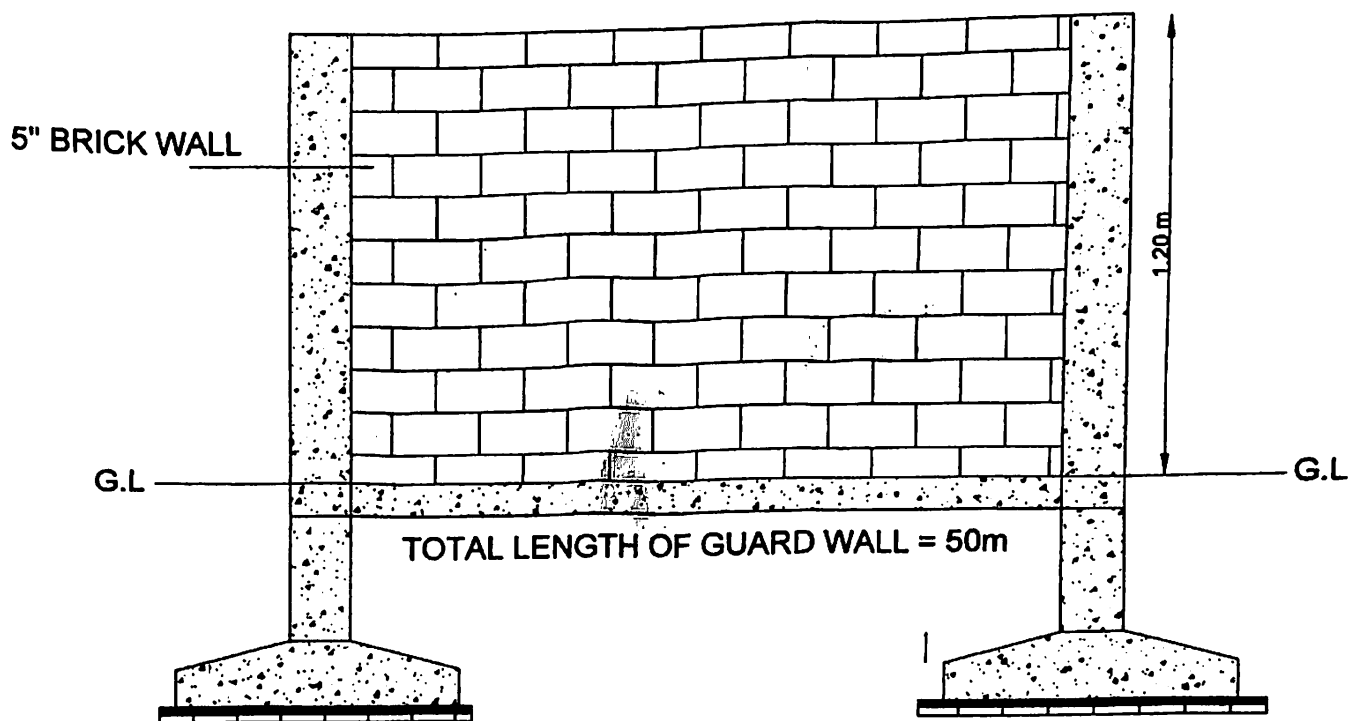

Not to Scale

CROSS-SECTION OF GUARD WALL

[Handwritten signature]
 Approved -
 With Date: 2026

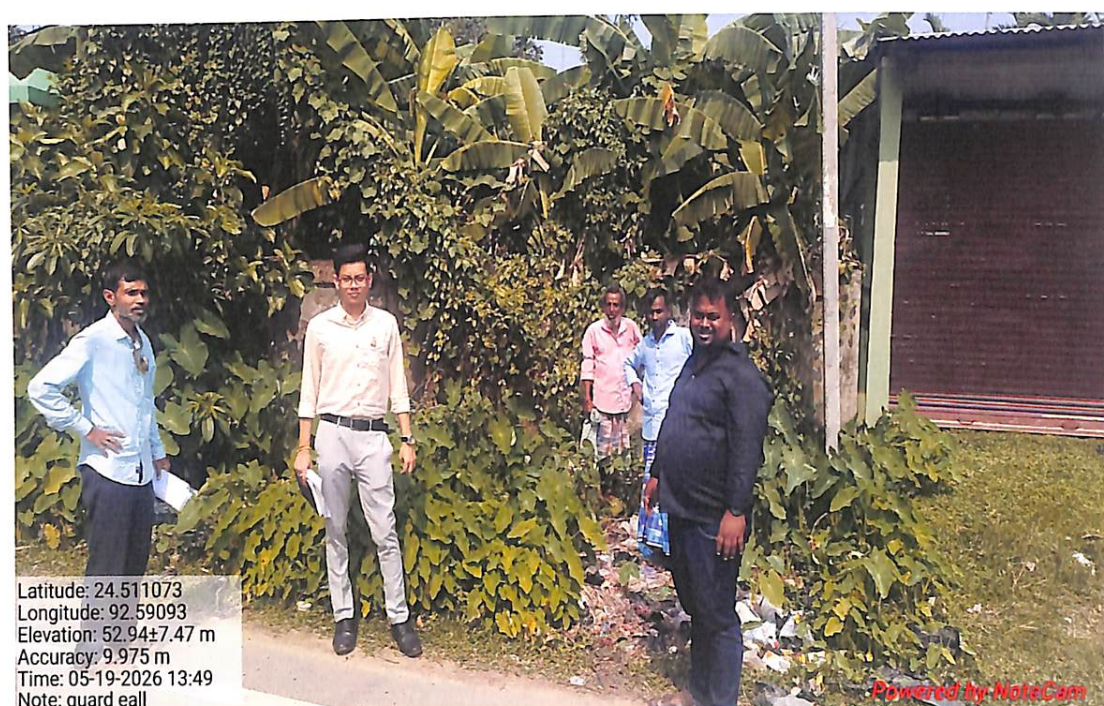

ENQUIRY / INVESTIGATION REPORT**I. SCHEME / WORK DETAILS**

Scheme / Work Name	Construction of Guard Wall on the South Side of Auditorium Hall at Village Mahammadpur-II, Group no.-3.
Fund Source	14 th Finance Commission (FY 2018-19)
Financial Year	2018-19
MLA Constituency	Katlicherra
District	Hailakandi, Assam
Sanctioned Amount (₹)	Rs. 5,50,000

II. BACKGROUND & ALLEGATIONS

2.1 The present enquiry was initiated pursuant to a complaint / reference alleging misappropriation of Government funds sanctioned under 14th Finance Commission (FY 2018-19) for the scheme "Construction of Guard Wall on the South Side of Auditorium Hall at Village Mahammadpur-II, Group no.-3" under Katlicherra MLA Constituency in the district of Hailakandi, Assam.

2.2 The specific allegations under enquiry are as follows:

(a) The guard wall has been constructed as a personal guard wall of Ex-MLA (Katlicherra) LAC

2.3 The complainant / referring authority is: Ex-MLA (Algapur) LAC

III. DOCUMENTS CALLED FOR & EXAMINED

Sl.	Document Description	Source / Office
1	Plan and estimate	O/o BDO, Lala
2	Work Order / Agreement with Contractor	Executing Agency
3	Measurement Books (MB)	Executing Agency
4	Completion / Utilization Certificate	Executing Agency
8	Photographs	Site

IV. FIELD INSPECTION FINDINGS

4.1 The Investigating Officer conducted a physical site inspection of the location at Mahmadpur Part-2, Group No.-3, Hailakandi district on19/5/26.

4.2 PHYSICAL STATUS OF THE AUDITORIUM BUILDING:

Upon physical inspection, it is found that the Guard wall on the south side of Auditorium Hall at the said location IS IN EXISTENCE. The following observations were made during the site inspection:

Observation Parameter	Findings / Remarks
Location / Address of Site	Mahmadpur Part-2, Group No.-3,Hailakandi
Structure Exists on Site	YES, Guard wall is present on the South Side of Auditorium. The Guard Wall was reconstructed in 2025, as the previous structure submerged due to Earth filling activities.
Apparent Stage of Construction	Completed
Quality of Construction (Visual)	Good
Name Board / Inscription Present	Present
Witnesses Present During Inspection	Present
Photographs Taken	Yes

V. FINANCIAL SCRUTINY

5.1 Amount sanctioned under MLA Untied Fund 2016-17 for this work: Rs. 5,50,000

5.2 Amount actually released / disbursed: Rs. 5,50,000

5.3 Remarks on Financial Irregularities (if any): none

VI. ANALYSIS& OBSERVATIONS

6.1 Based on the documents examined, site inspection, and statements recorded, the following observations are made:

(a) The Guard Wall on the south side of auditorium hall at Mahammadpur Part-2 is physically present at the site and is verifiable on ground.

(b) The auditorium hall lies near the personal residence of Ex-MLA (Katlicherra) LAC, so the guard wall constructed on south side also covers the MLA's personal residence.

VII. LIST OF ANNEXURES

Annexure	Description
A	Plan and estimate
B	Photographs taken during site inspection
C	Locals present during site inspection

Signature: *Dr. Raj Prasanna Aleman*

Place: *Hailakandi*

Date: *22/05/26* . Assistant Commissioner
Hailakandi



GOVERNMENT OF ASSAM
OFFICE OF THE BLOCK DEVELOPMENT OFFICER
LALA DEVELOPMENT BLOCK

Estimate

DISTRICT	:- HAILAKANDI
Name of G.P.	:- Mahammedpur Joykrishnapur G.P
Name of Block	:- Lala Development Block
PROGRAMME	:- 14th Finance Commission 2016-17 (1st. inst.).
NAME OF WORKS	:- Construction of RCC Guard Wall for community water pond near the house of Rahim Uddin at vill. – Mahammedpur part-II.
ESTIMATED COST	:- Rs. 400000.00

14

GOVERNMENT OF ASSAM
OFFICE OF THE BLOCK DEVELOPMENT OFFICER
LALA DEVELOPMENT BLOCK

Name of District :- Hailakandi
Name of Block :- Lala Development Block
Name of G.P. :- Mahammedpur Joykrishnapur G.P
Name of work :- Construction of RCC Guard Wall for community water pond near the house of Rahim Uddin at vill. - Mahammedpur part-II.
Estimated Amount :- 400000.00


Report

It is essential to provide Guard Wall to protect the community water pond .
Considering the necessity of the work the Scheme has been taken up in Goan Sobha under 14th Assam financial Commission .


As per Instruction of higher Authority the Estimate has been framed to show the probable cost of the work. As per as possible work will be executed by engaging local labour to assist them financially in this lien Season .

The rate of this estimate has been quoted from SOR 2013-14 APWD(Building) and SOR (RR) PWRD Assam 2018-19 . As trend of GST a premium of 7% has been added as per the latter of Superintending Engineer P.W.D Building , Silchar Circle. As per norms 10% being deducted as Contractor's profit & 2% is added as Contingency .

All the works will be carried out as per A.P.W.D general specifications current in the state . following all the Guidelines of 14th F.C and by observing all instructions and formalities of the P&RD department time to time .


BDO Lala Dev. Block
BLOCK DEV. OFFICER
LALA DEV. BLOCK

GP Secy.


Accredited
L.

GOVT. OF ASSAM

Dist Hailakandi

7th Floor

Detail estimate of Guard Wall (Length 40.00m and Height 1.20m)

Name of Work :

Construction of RCC Guard Wall for community water pond near the house of Rahim Uddin at Vill : Mohammed part-II

Item No	Particulars	NH	I	B	H	Qty	Unit	Rate (Rs)	Amount
---------	-------------	----	---	---	---	-----	------	-----------	--------

1/1 1 Earthwork in excavation in foundation structures of wall, column etc including refilling after completion of work

Footling	21.00	1.50	1.50	1.75	82.89
Tie Beam	1.00	40.00	0.25	0.25	2.50
(-) Deduction for Post	21.00	0.25	0.25	0.25	0.33

84.88 Cum 108.82 9234.49

2/4 1 Providing setting in foundation and under floor with stone/brick quality picked jama brick sand pack and laid to level in panel after preparing the sub grade as directed including all labour and materials and if necessary dewatering complete. (Flat brick setting)

Footling	21.00	1.50	1.00	47.25
Tie Beam	1.00	40.00	0.25	10.00
(-) Deduction for Post	21.00	0.25	0.25	1.31

55.94 Cum 268.71 20024.72

16

Providing concrete for
plain/reinforced
concrete in open
foundations complete
as per drawings and
technical specifications
3/11.4 Clause 802, 803, 1202
& 1203

B) With natural Gravel
III) P.C.C. Grade M20
Nominal Mix 1:2:4 (Hand Mix)

Footings	21.00	1.50	1.50	0.08	3.54		
Tie Beam	1.00	40.00	0.25	0.08	0.75		
(-)Deduction for Post	21.00	0.25	0.25	0.08	0.10		
					4.20	Cum 5543.90	23258.39

Supplying, fitting and
placing TMT (Fe-500
D) reinforcement bar
(From Primary
Producer:
TATA/SAIL/Essex
Steel/ Jindal
steel/Shyam
steel/RINL) in
substructure complete
as per drawings and
technical specification
Clauses 1002, 1005,
1010 & 1202

4/12.6

Tie Beam 12mm dia
Post 12mm dia
Footings Base 10mm
dia @ 100mm c/c
8mm stirrups for
Beam@125mm c/c
8mm stirrups for
Post@125mm c/c

	1.00	40.00	4.00	0.89	142.40
	21.00	2.00	4.00	0.89	149.52
	21.00	1.35	28.00	0.62	492.16
	1.00	321.00	0.90	0.40	114.12
	21.00	13.00	0.78	0.40	85.18
					983.37

Add 5% for Lapping 1032.54 Kg
1.03 Ton 56373.70 58207.87

5/12.6 Plain/reinforced
cement concrete in
substructure complete
as per drawings
and technical
specification Clauses
802, 804, 805, 808,
807, 1202 and 1204
A) With crushed stone
IV) R.C.C grade M 20

Tie Beam	1.00	40.00	0.25	0.25	2.50
Post	21.00	0.75	0.25	0.25	0.98
Trapezoidal Section	21.00	0.58	1.45	0.25	4.42
Footling Base	21.00	1.45	1.45	0.35	15.45

23.35 Cum 7073.00 165175.77

8/13.2 Supplying, fitting and
placing TMT (Fe-500D)
reinforcement bar .
(From Primary
Producer :TATA/
SAIL/EssexSteel/Jindal
steel/Shyamsteel/RINL
) In
superstructure
complete as per
drawing and technical
specifications
Clauses 1002, 1010
and 1202

Post 12mm dia	21.00	1.20	4.00	0.89	89.71
8mm stirrups for Post@125mm c/c	21.00	11.00	0.43	0.40	39.24

128.95 Kg

Add 5% for Lappage 135.39 Kg

0.14 Ton 57715.00 7814.31

7/13.1 Providing and laying
reinforced cement
concrete in super
structure as per
drawing and technical
specifications Clauses
800, 1205.4 and
1205.5
A) With crushed stone
II) R.C.C Grade M20

Post above Tie Beam	21.00	0.15	0.15	1.20	0.57
---------------------	-------	------	------	------	------

0.57 Cum 7879.55 4354.30



Providing formwork of ordinary timber planking so as to give a rough finish including centering, shuttering, strutting and propping etc. and removal of the same of in-situ reinforced concrete and plain concrete work in; (Using 25mm Tie Beam

8

	2.00	40.00	0.25	20.00
	84.00	0.75	0.25	15.75
Post	84.00	1.20	0.15	15.12
Trapezoidal Section	84.00	1.45	0.25	30.45
Base	84.00	1.45	0.35	42.63

123.95 Sqm 252.24 31265.15

Brick masonry work in cement mortar in foundation complete excluding pointing and plastering as per drawing and technical specifications Clauses 600, 1202 & 1203

9/11.5

I. Brick masonry in 1:3 cement mortar	1.00	40.00	0.13	1.20	6.00
(-)Deduction for Post	21.00	0.15	0.15	0.13	0.06

5.94 Cum 6807.30 40441.74


Plastering with cement mortar (1:4), 15 mm thick on brick work in substructure as per technical specification Clauses 613.4 & 1204

10/12.
3

Brick Wall plaster	2.00	40.00	1.20	96.00
Brick Wall top plaster	1.00	40.00	0.13	5.00

101.00 sqm 129.57 13086.57

19



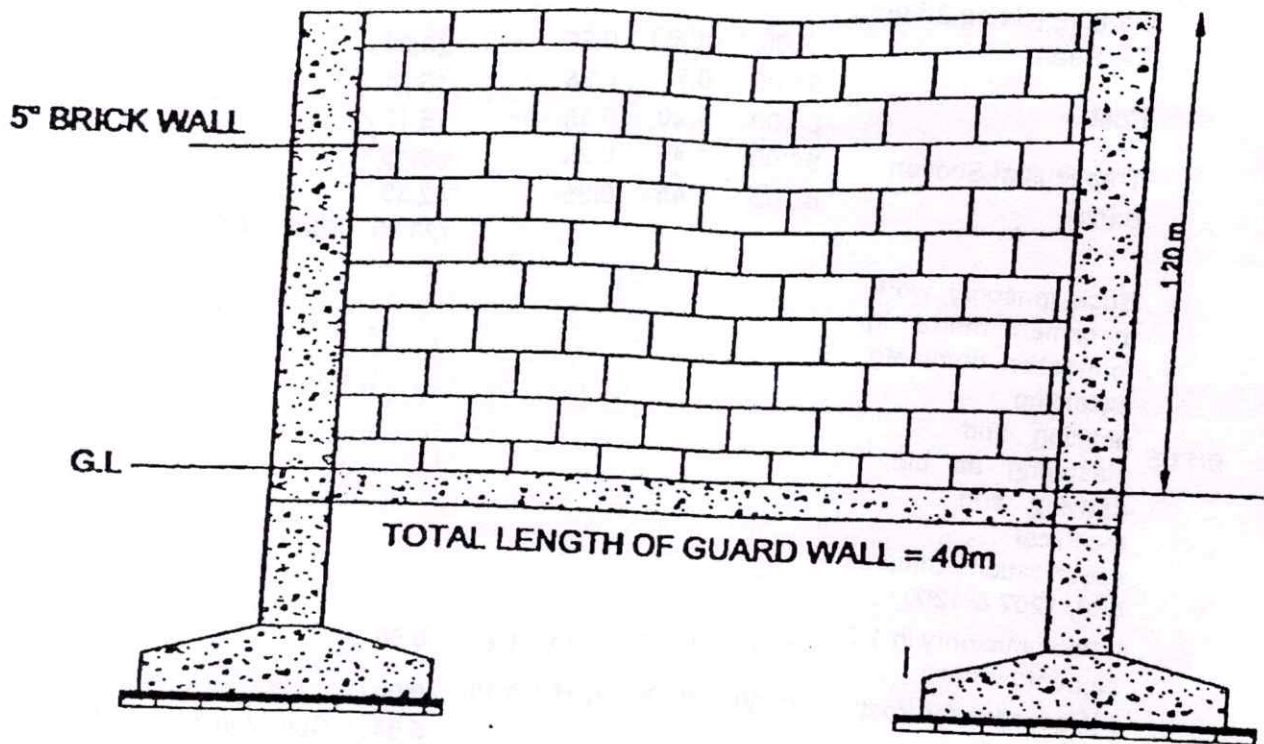


Not to Scale

CROSS-SECTION OF GUARD WALL

[Signature]
 J. ASSTT (NOBOJYOTI) DEV-HKD, JR.
 District Administrative Assistant, DC Office Hailakandi

20

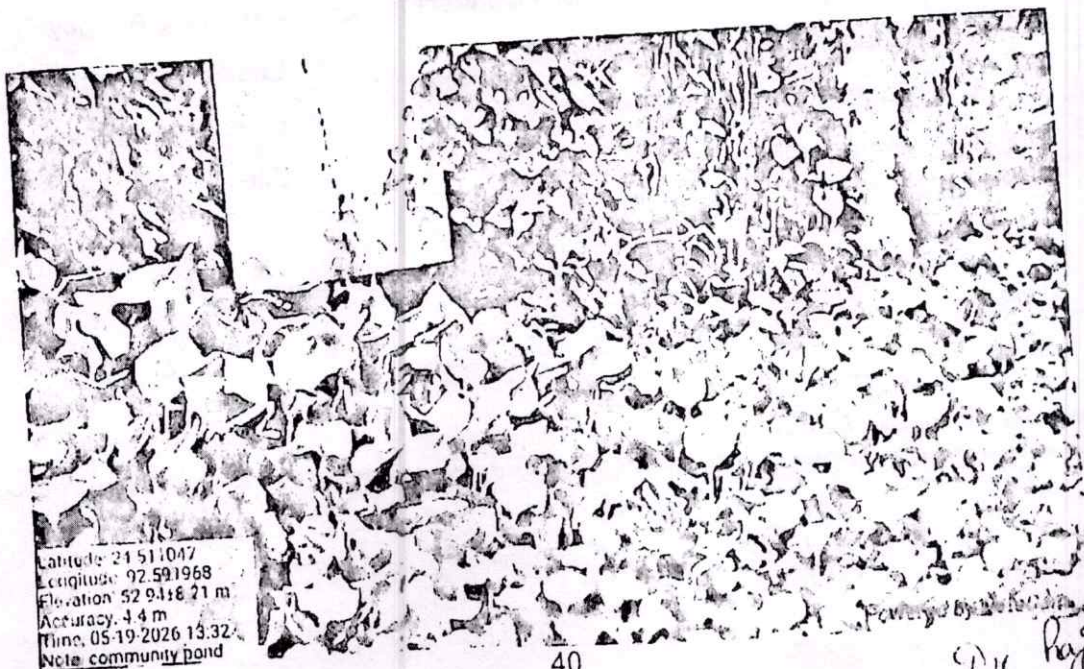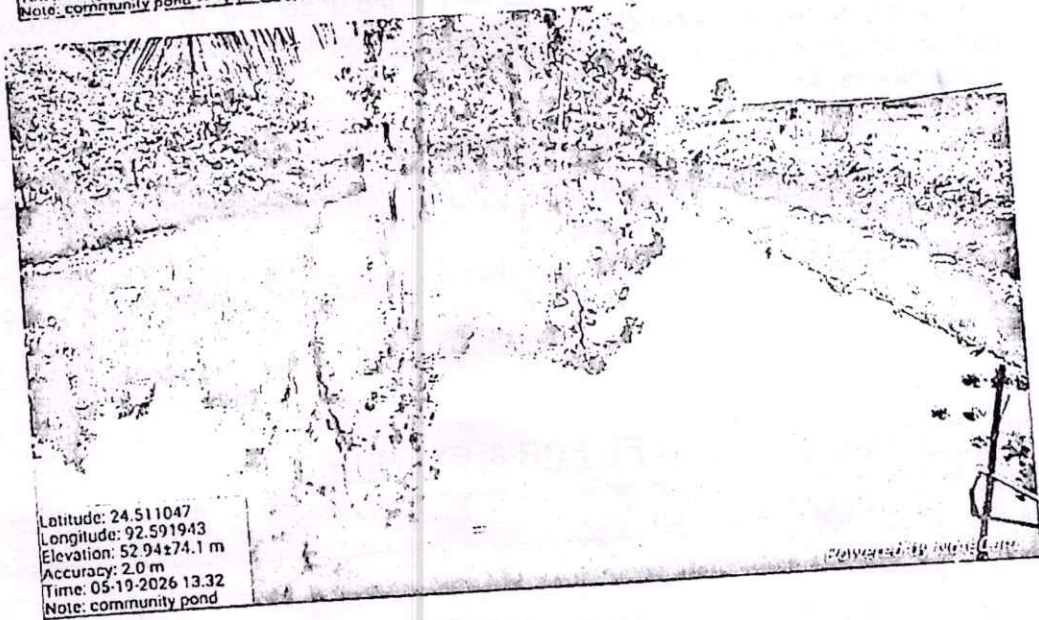

21

Dr. Raj Prasad

Assistant Comm

on 24/07/2026 06:11

Hailakandi

ENQUIRY / INVESTIGATION REPORT

I. SCHEME / WORK DETAILS

Scheme / Work Name	Construction of RCC Guard Wall for Community Water Pond near the house of Rahim Uddin at Village Mohammadpur Part-2, Group No.-3.
Fund Source	14 th Finance Commission (FY 2016-17)
Financial Year	2016-17
MLA Constituency	Katlicherra
District	Hailakandi, Assam
Sanctioned Amount (₹)	Rs. 4,00,000/-

II. BACKGROUND & ALLEGATIONS

2.1 The present enquiry was initiated pursuant to a complaint / reference alleging misappropriation of Government funds sanctioned under the 14th Finance Commission (FY 2016-17) for the scheme "Construction of RCC Guard Wall for Community Water Pond near the house of Rahim Uddin at Village Mohammadpur Part-2, Group No.-3" under Katlicherra MLA Constituency in the district of Hailakandi, Assam.

2.2 The specific allegations under enquiry are as follows:

(a) specified RCC Guard Wall has been constructed for the personal pond of Ex-MLA Katlicherra LAC

2.3 The complainant / referring authority is: Ex-MLA Algapur LAC

III. DOCUMENTS CALLED FOR & EXAMINED

Sl.	Document Description	Source / Office
1	Plan and estimate	O/o BDO, Lala
2	Work Order / Agreement with Contractor	Executing Agency
3	Measurement Books (MB)	Executing Agency
4	Completion / Utilization Certificate	Executing Agency
8	Photographs	Site

22

IV. FIELD INSPECTION FINDINGS

4.1 The Investigating Officer conducted a physical site inspection of the location at Mahmadpur Part-2, Hailakandi district on 19/5/26.

4.2 PHYSICAL STATUS OF THE RCC GUARD WALL:

Upon physical inspection, it is found that the RCC Guard Wall at the said location IS IN EXISTENCE. The following observations were made during the site inspection:

Observation Parameter	Findings / Remarks
Location / Address of Site	Mahmadpur Part-II, Hailakandi
Structure Exists on Site	YES — Guard wall observed at site. The community pond lies in close proximity of the residence of the EX-MLA. But the pond is being used by locals of the area for day-to-day activities.
Apparent Stage of Construction	Completed
Quality of Construction (Visual)	Good
Name Board / Inscription Present	Present
Witnesses Present During Inspection	Present
Photographs Taken	Yes

V. FINANCIAL SCRUTINY

- 5.1 Amount sanctioned under MLA Untied Fund 2016-17 for this work: ₹ 4,00,000
 5.2 Amount actually released / disbursed: ₹ 4,00,000
 5.3 Remarks on Financial Irregularities (if any): none

VI. ANALYSIS & OBSERVATIONS

6.1 Based on the documents examined, site inspection, and statements recorded, the following observations are made:

(a) The RCC Guard Wall for Community Water Pond at Mahammadpur Part-2 is physically present at the site and is verifiable on ground.

(b) The Community Water Pond lies within close proximity of the Ex-MLA (Katlicherra) LAC, although it's being used by locals for daily activities. The RCC Guard Wall is thereby in place.

23

VII. LIST OF ANNEXURES

Annexure	Description
A	Plan and estimate
B	Photographs taken during site inspection
C	Locals present during site verification

Signature: Dr. Raj Prasanna Aleman

Place: Hailakandi

Date: 22/05/26

Assistant Commissioner
Hailakandi

24



GOVERNMENT OF ASSAM
OFFICE OF THE BLOCK DEVELOPMENT OFFICER
LALA DEV. BLOCK: HAILAKANDI

PLAN & ESTIMATE

NAME OF WORK: - RENOVATION OF COMMUNITY POND WITH GUARD WALL NEAR REAL LINE AT VILLAGE MAHAMMEDPUR PART II(PHASE II)
(GROUP NO.3) UNDER 15TH FC, 2020-21/ 1ST INSTALL/ TIED GRANT

T.S No-


NAME OF DISTRICT :- HAILAKANDI
NAME OF DEV. BLOCK:-LALA
NAME OF THE GP:- MAHAMMEDPUR JOYKRISHNAPUR GP
IMPLEMENTING AGENCY:- MAHAMMEDPUR JOYKRISHNAPUR GP
ESTIMATED AMOUNT :-RS. 3,75,634.00
PROPOSED PERIOD FOR COMPLETION OF WORK:-

25


OFFICE OF THE MAHAMMEDPUR JOYKRISHNAPUR G.P

NON-DUPPLICACY CERTIFICATE & FEASIBILITY

Certified that the scheme – “Renovation of community pond with guard wall near real line at village Mahammedpur part II[phase II] (Group No.3) under 15TH FC,2020-21/ 1st Install/ Tied Grant” is Genuine, feasible and need Based. This will serve the people living on nearby areas. There is no such other scheme have taken up from any other Programme. It is also certify that the scheme is not overlapped by any other projects of any other programme. The requisite land and space are also available for implementation of this project. We have thoroughly discussed on this matter. So, there is no objection on the land owner & Villagers for this purpose.



G.P secretary
Mahammedpur Jaikrishnapur G.P
Secretary
Mahammedpur-Joykrishnapur G.P.



Lala Development Block

26

Work-Renovation of community pond with guard wall near real line at village
pur part II[phase II] (Group No.3) under 15TH FC,2020-21/ 1st install/ Tied Grant

DISTRICT:- HAILAKANDI

of Dev. Block:-LALA

me of GP:-MAHAMMEDPUR JOYKRISHNAPUR

Implementing Agency:-MAHAMMEDPUR JOYKRISHNAPUR

Estimated Amount: Rs 3,75,634.00

Proposed Period for Completion of Work:-

REPORT OF ESTIMATE

This detailed estimate amounting to Rs.3,75,634.00 (Rupees Three lakh) only has been framed to show the probable cost of Renovation of community pond with guard wall near real line at village Mahammedpur part II[phase ii] (Group No.3) under 15TH FC,2020-21/ 1st install/ Tied Gran

The work has been taken up from GPDP which is duly approved and prioritized by the Gaon Sabha and is found feasible for execution and there is no duplicity.

Objectives of the Scheme

- 1.To provide employment to the local people who are willing to do manual labour for their livelihood during lean season
2. Rain water gets harvested naturally by the pond, gets stored up, recharging the ground water and serving as an indicator of the water table in the village. etc.

The estimate has been prepared as per the rate of APWD-SOR(RR)-2020-21. As per norms 12.5% being deducted as Contractor's profit ,as the work will be executed departmentally.

All the works will be carried out as per Govt. rules current in the state, following all the Guidelines of 15th FC and by observing all instructions and formalities of the P & R.D. department time to time.

Secretary

Manammedpur-Joykrishnapur G.P.

Accredited Engineer
Lala Dev. Block

27

Personnel

ABSTRACT OF COST

Name of The Work:-Renovation of Community Pond with Guard Wall near rail Line at Village Mahammedpur part ii , Phase-2 at Group No-3

Sl No	Item	Amount in Rs.
1	Construction of a Community Water Harvesting Tank	376983.64
	Deduct 12.5 % for Overheads and Contractors profits	47122.96
	Total cost of work	329860.69
	Add 12.5% for GST 12%	41232.59
	Add Sign Board	4540.00
	Grand Total	375633.27
		Say Rs.3,75,634
(Rupees Three Lakhs Seventy Five Thousand Six Hundred Thirty Four) Only		

39583.28

5000.00

3,74,443.97

Accredited Engineer
Lala Dev Block

Rs. 3,75,634/-
three lac
seventy five thousand six -
hundred thirty four) only
S. No. 697 Reg 1
d. 06-06-2022

Checked
06/06/22
Junior Engineer
Lala Development Block

08/06/2022
Lala Development Block

28

Name of Work:- Renovation of Community Pond with Guard Wall near rail line at Village Mahammedpur part II, Phase-2 at Group No-3 Pond Ghat width=2.50m and G/Wall Length=24.00m & height=1.20m (The Estimate is prepared as per APWRD SOR 2020-21)									
Item No	Particulars	No	L	B	H	Qty	Unit	Rate (Rs.)	Amount
1/11.1	Earthwork in excavation for structures as per drawing and technical specifications Clause 305.1 including setting out, construction of shoring and bracing, removal of stumps and other deleterious material and disposed upto a lead of 50 m, dressing of sides and bottom and backfilling in trenches with excavated suitable material. V) Murshy Soil Up to 3.00 m Depth								
	Footing for ghat	6.00	1.50	1.50	2.10	28.35			
	Tie Beam for ghat	1.00	10.00	0.25	0.25	0.63			
	Footing for wall	13.00	1.50	1.50	1.75	51.19			
	Tie Beam for wall	1.00	24.00	0.25	0.25	1.50			
	(-)Deduction for Post ghat	6.00	0.25	0.25	0.25	0.09			
	(-)Deduction for Post wall	13.00	0.25	0.25	0.25	0.20			
						81.37	Cum	518.20	42163.67
2/4.1.1 (CIVIL SOR 2013- 14)	Providing soling in foundation and under floor with stone/best quality picked jama brick sand pack and laid to level in panel after preparing the sub grade as directed including all labour and materials and if necessary dewatering complete. (Flat brick soling)								
	Footing for ghat	6.00	1.50	1.50		13.50			

	Tie Beam for ghat	1.00	10.00	0.25		2.50			
	Footing for wall	13.00	1.50	1.50		29.25			
	Tie Beam for wall	1.00	24.00	0.25		6.00			
	(-)Deduction for Post ghat	6.00	0.25	0.25		0.38			
	(-)Deduction for Post wall	13.00	0.25	0.25		0.81			
						50.06	Sqm	368.71	18458.54
3/11.4	Providing concrete for plain/reinforced concrete in open foundations complete as per drawings and technical specifications Clause 802, 803, 1202 & 1203 B) With natural Gravel III) P.C.C. Grade M20 Nominal Mix 1:2:4 (Hand Mix)								
	Footing for ghat	6.00	1.50	1.50	0.20	2.70			
	Tie Beam for ghat	1.00	10.00	0.25	0.20	0.50			
	Footing for wall	13.00	1.50	1.50	0.08	2.19			
	Tie Beam for wall	1.00	24.00	0.25	0.08	0.45			
	(-)Deduction for Post ghat	6.00	0.25	0.25	0.20	0.08			
	(-)Deduction for Post wall	13.00	0.25	0.25	0.20	0.16			
						5.61	Cum	5543.90	31080.49
4/12.6	Supplying, fitting and placing TMT (Fe-500 D) reinforcement bar (From Primary Producer: TATA/SAIL/Essex Steel/ Jindal steel/Shyam steel/RINL) in substructure complete as per drawings and technical specification Clauses 1002, 1005, 1010 & 1202								
	Tie Beam 12mm dia	1.00	34.00	4.00	0.89	121.04			
	Post 12mm dia	19.00	2.39	4.00	0.89	161.66			
	Footing Base 10mm dia @ 100mm c/c	19.00	1.35	28.00	0.62	445.28			
	8mm stirrups for Beam@125mm c/c	1.00	272.00	0.90	0.40	96.70			
	8mm stirrups for Post@125mm c/c	19.00	15.00	0.78	0.40	88.92			
						913.60			
	Add 5% for Lapping					959.28	Kg		

30

						0.96	Ton	56373.70	54078.14
5/13.1	Plain/reinforced cement concrete in substructure complete as per drawings and technical specification Clauses 802, 804, 805, 806, 807, 1202 and 1204 A) With crushed stone IV) R.C.C grade M 25 I) Height upto 5 M								
	Tie Beam	1.00	34.00	0.25	0.25	2.13			
	Post	19.00	1.25	0.25	0.25	1.48			
	Trapezoidal Section	19.00	0.60	0.60	0.25	1.71			
	Footing Base	19.00	1.50	1.50	0.35	14.96			
						20.28	Cum	7073.00	143453.70
6/13.2	Supplying, fitting and placing TMT (Fe-500D) reinforcement bar. (From Primary Producer :TATA/ SAIL/ Essar Steel/ Jindal Steel/ Hyam Steel/ RINL) in superstructure complete as per drawing and technical specifications Clauses 1002, 1010 and 1202								
	Post 12mm dia	19.00	1.20	4.00	0.89	81.17			
	8mm stirrups for Post @ 125mm c/c	19.00	12.00	0.58	0.40	52.23			
						133.40	Kg		
						140.07	Kg		
						0.13	Ton	57715.00	7699.34
7/13.1	Providing and laying reinforced cement concrete in super structure as per drawing and technical specifications Clauses 800, 1205.4 and 1205.5 A) With crushed stone II) R.C.C grade M 25 a) Height upto 5 M								
	Post above Tie Beam	19.00	0.15	0.15	1.20	0.51			
						0.51	Cum	7679.55	3939.61


8	Providing formwork of ordinary timber planking so as to give a rough finish including centering, shuttering, strutting and propping etc. and removal of the same of in-situ reinforced concrete and plain concrete work in; (Using 25mm thick plank)								
	Tie Beam	3.00	34.00	0.25		25.50			
		76.00	1.50	0.25		28.50			
	Post	76.00	1.20	0.15		13.68			
		76.00	1.50	0.25		28.50			
	Trapezoidal Section	76.00	1.50	0.25		28.50			
	Base	76.00	1.50	0.35		39.90			
						136.08	Sqm	252.24	34324.82
9/11.5	Brick masonry work in cement mortar in foundation complete excluding pointing and plastering as per drawing and technical specifications Clauses 600, 1202 & 1203								
	I. Brick masonry in 1:3 for ghat	1.00	10.00	0.13	1.20	1.50			
	I. Brick masonry in 1:3 for G/Wall	1.00	24.00	0.13	1.20	3.60			
	(-)Deduction for Post	19.00	0.15	0.15	1.20	0.51			
						4.59	Cum	6807.30	31225.09
10/12.3	Plastering with cement mortar (1:4), 15 mm thick on brick work in substructure as per technical specification Clauses 613.4 & 1204								
		2.00	10.00	1.20		24.00			
	Brick Wall	1.00	10.00	0.13		1.25			
		1.00	24.00	1.20		28.80			
						54.05	sqm	129.57	7003.26

32


11/3.4	Construction of embankment with approved material obtained from borrow pits with a lift upto 1.5m, transporting to site, spreading, grading to required slope and compacting to meet requirement of Tables 300.1 and 300.2 with a lead upto 1000 m as per Technical Specification Clause 501.5 (i) Govt. Land								
	Earth work in filling	1.00	20.50	0.47	1.20	14.85			9596.27
						14.86	cum	228.30	376963.64
Total Cost of Civil works as per FOR 2020-21 of Grand Total									


 District Administrative Assistant
 District Office Hailakandi


 District Administrative Assistant
 District Office Hailakandi

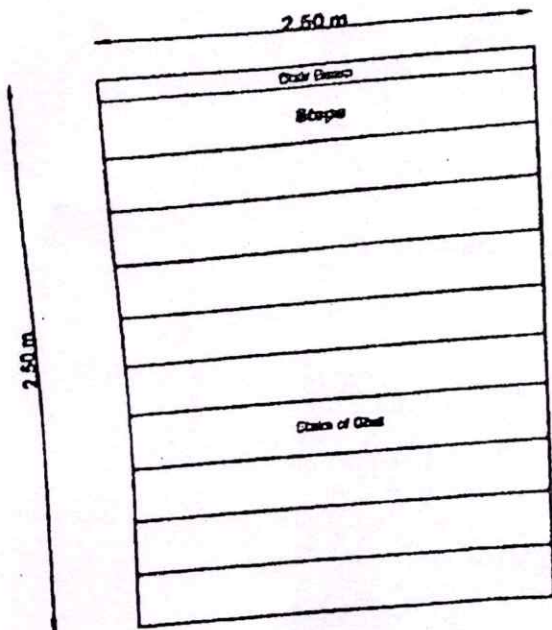





Plan of Ghat

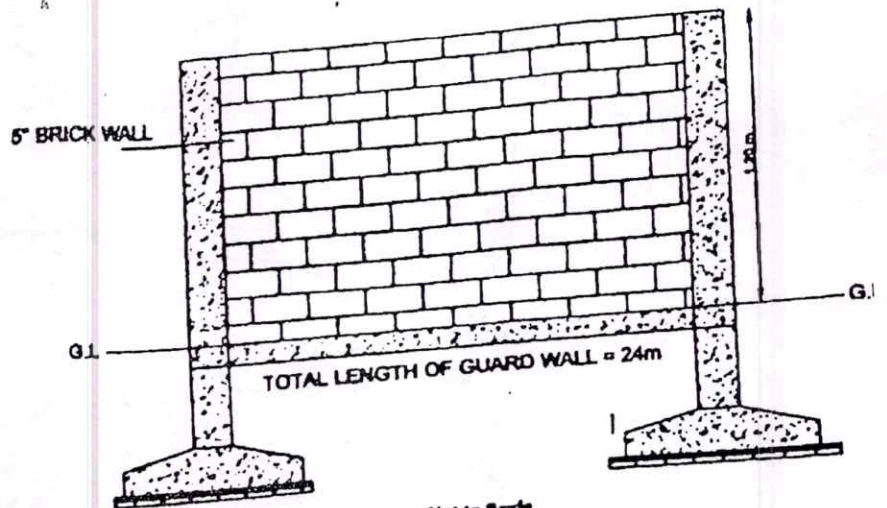

CROSS-SECTION OF GUARD WALL

[Signature]
 Approved Engineer
 Date: 24.07.2026

34

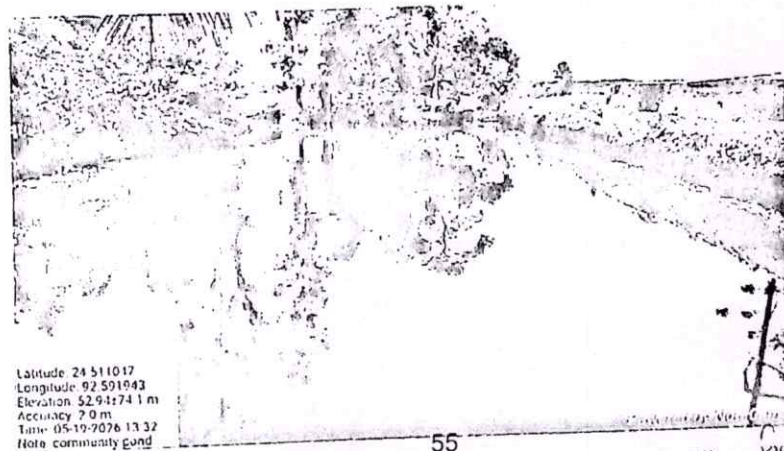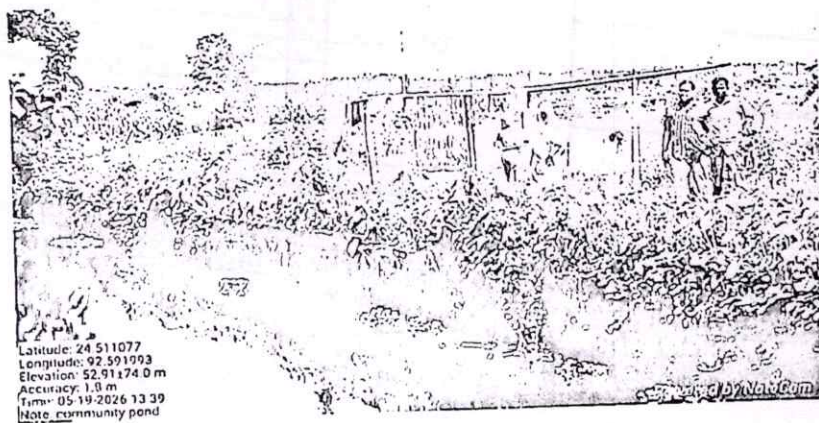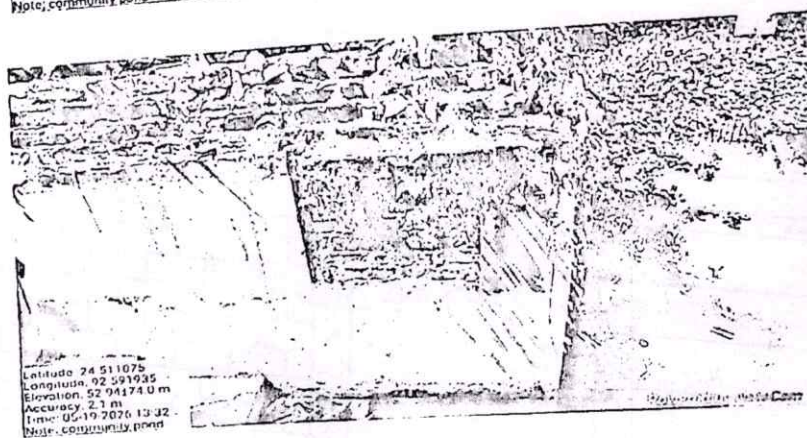

35

Puranna Allemar
Assistant Commissioner
Hailakandi

ENQUIRY / INVESTIGATION REPORT

I. SCHEME / WORK DETAILS

Scheme / Work Name	Renovation of Community Pond with Guard Wall near Rail Line at Village Mohammadpur Part-2 (Phase-II), Group No.-3.
Fund Source	15 th Finance Commission (FY 2020-21)
Financial Year	2020-21
MLA Constituency	Katlicherra
District	Hailakandi, Assam
Sanctioned Amount (₹)	Rs. 3,75,634

II. BACKGROUND & ALLEGATIONS

2.1 The present enquiry was initiated pursuant to a complaint / reference alleging misappropriation of Government funds sanctioned under the 15th Finance Commission (FY 2020-21) for the scheme "Renovation of Community Pond with Guard Wall near Rail Line at Village Mohammadpur Part-2 (Phase-II), Group No.-3" under Katlicherra MLA Constituency in the district of Hailakandi, Assam.

2.2 The specific allegations under enquiry are as follows:

(a) specified Guard Wall has been constructed in the personal pond of Ex-MLA (Katlicherra) LAC

2.3 The complainant / referring authority is: Ex-MLA Alqapur LAC

III. DOCUMENTS CALLED FOR & EXAMINED

Sl.	Document Description	Source / Office
1	Plan and estimate	O/o BDO, Lala
2	Work Order / Agreement with Contractor	Executing Agency
3	Measurement Books (MB)	Executing Agency
4	Completion / Utilization Certificate	Executing Agency
8	Photographs	Site

IV. FIELD INSPECTION FINDINGS

4.1 The Investigating Officer conducted a physical site inspection of the location at Mahmadpur Part-2, Hailakandi district on 19/5/26.

4.2 PHYSICAL STATUS OF THE GUARD WALL:

Upon physical inspection, it is found that the guard wall at the said location **IS IN EXISTENCE**. The following observations were made during the site inspection:

Observation Parameter	Findings / Remarks
Location / Address of Site	Mahammadpur Part-II, Hailakandi
Structure Exists on Site	YES — Guard Wall is present. The community pond lies in close proximity of the residence of the EX-MLA. But the pond is being used by locals of the area for day-to-day activities.
Apparent Stage of Construction	Completed
Quality of Construction (Visual)	Good
Name Board / Inscription Present	Not found
Witnesses Present During Inspection	Present
Photographs Taken	Yes

V. FINANCIAL SCRUTINY

- 5.1 Amount sanctioned under MLA Untied Fund 2016-17 for this work: ₹ 3,75,634
- 5.2 Amount actually released / disbursed: ₹ 3,75,634
- 5.3 Remarks on Financial Irregularities (if any): none

VI. ANALYSIS & OBSERVATIONS

6.1 Based on the documents examined, site inspection, and statements recorded, the following observations are made:

- (a) The renovated RCC Guard Wall for Community Water Pond at Mahammadpur Part-2 is physically present at the site and is verifiable on ground
- (b) The Community Water Pond lies in close proximity of the residence of the Ex-MLA (Katlicherra) LAC, although it's being used by locals for daily activities.

(31)

VII. LIST OF ANNEXURES

Annexure	Description
A	Plan and estimate
B	Photographs taken during site inspection
C	Locals present during site inspection

Signature: *Dr. Raj Prasanna Aleman*

Place: *Hailakandi*

Date: *22/05/26* Assistant Commissioner
Hailakandi

38

Locals present during inspection-

1. AtikurRahmanLaskar (6002235263)
2. NizamUddinLaskar (9435178930)
3. Rahim Uddin (9954785383)

39
